

TKO - Soirée d'information

TKO - Information evening

Partie 1/ Part 1

Avancées du chantier

Site progress update

Jean-Yves Coulot

Membre du Comité Développement & Directeur du Board


Development Committee Member & Board Director

20 Février 2017

20 February 2017


Répartition actuelle de nos campus

Current distribution of our campuses

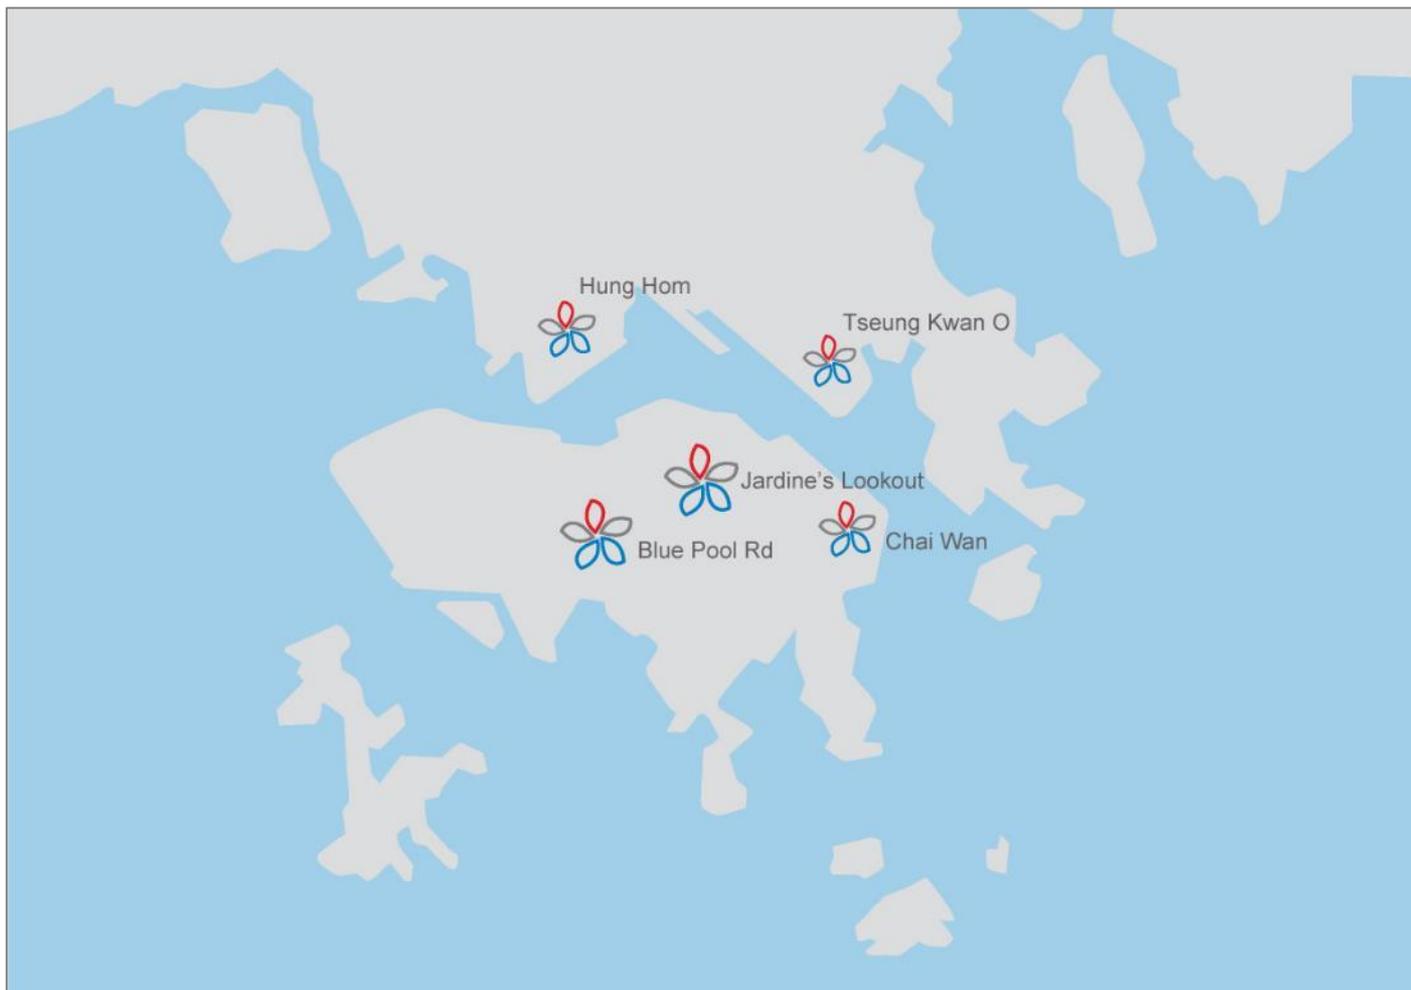

Localisation de Tseung Kwan O

Tseung Kwan O localisation

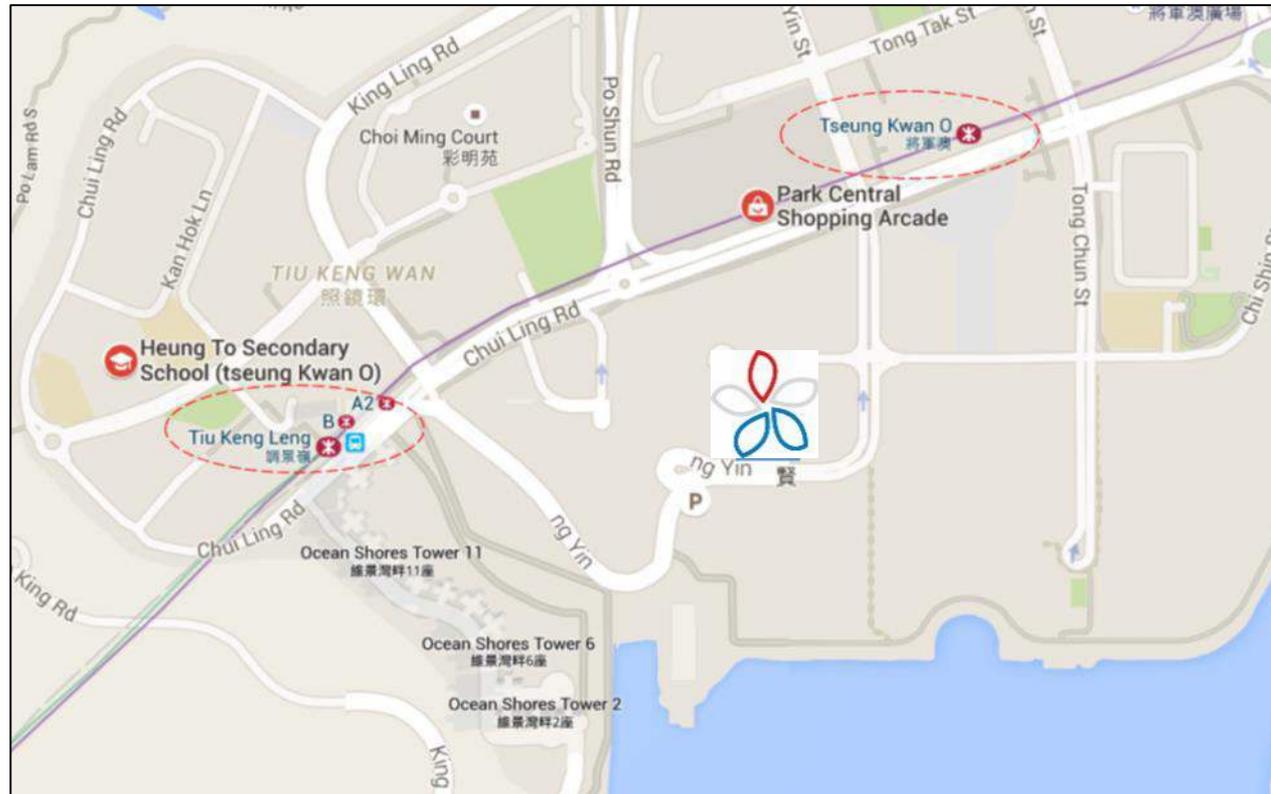

TKO Project Progress Update

Site Photos:



Photo 1- Site View (Oct 16) –
Piling completed



Photo 2- Site View (Nov 16) –
Pile load tests completed

TKO Project Progress Update

Site Photos:



Photo 3- Site View (Dec 16)
Pile cap Installation



Photo 4- Bird Eye View (Jan 17) –
Primary School Foundation Completion

TKO Project Progress Update

Site Photos:



[Photo 5- Site View \(17 Feb 16\)](#)

[Secondary School Foundation Completion with Site Handover to Main Contractor](#)

TKO Project Progress Update

Site Photos:



Photo 6- Tower crane erection (Jan 17)



Photo 7- FIS Hoarding at the Site Entrance (Jan 17)

TKO Project Progress Update

Site Photos:



Photo 8- Drainage construction in Progress (Feb 17)



Photo 9- Secondary School/ Covered Playground
Foundation Completion (Feb 17)

TKO Project Progress Update Bai Sun Ceremony 9 Feb 2017



TKO Project Progress Update Bai Sun Ceremony 9 Feb 2017




TKO Project Progress Update Bai Sun Ceremony 9 Feb 2017



TKO Project Progress Update

Overall Programme

Overall Programme

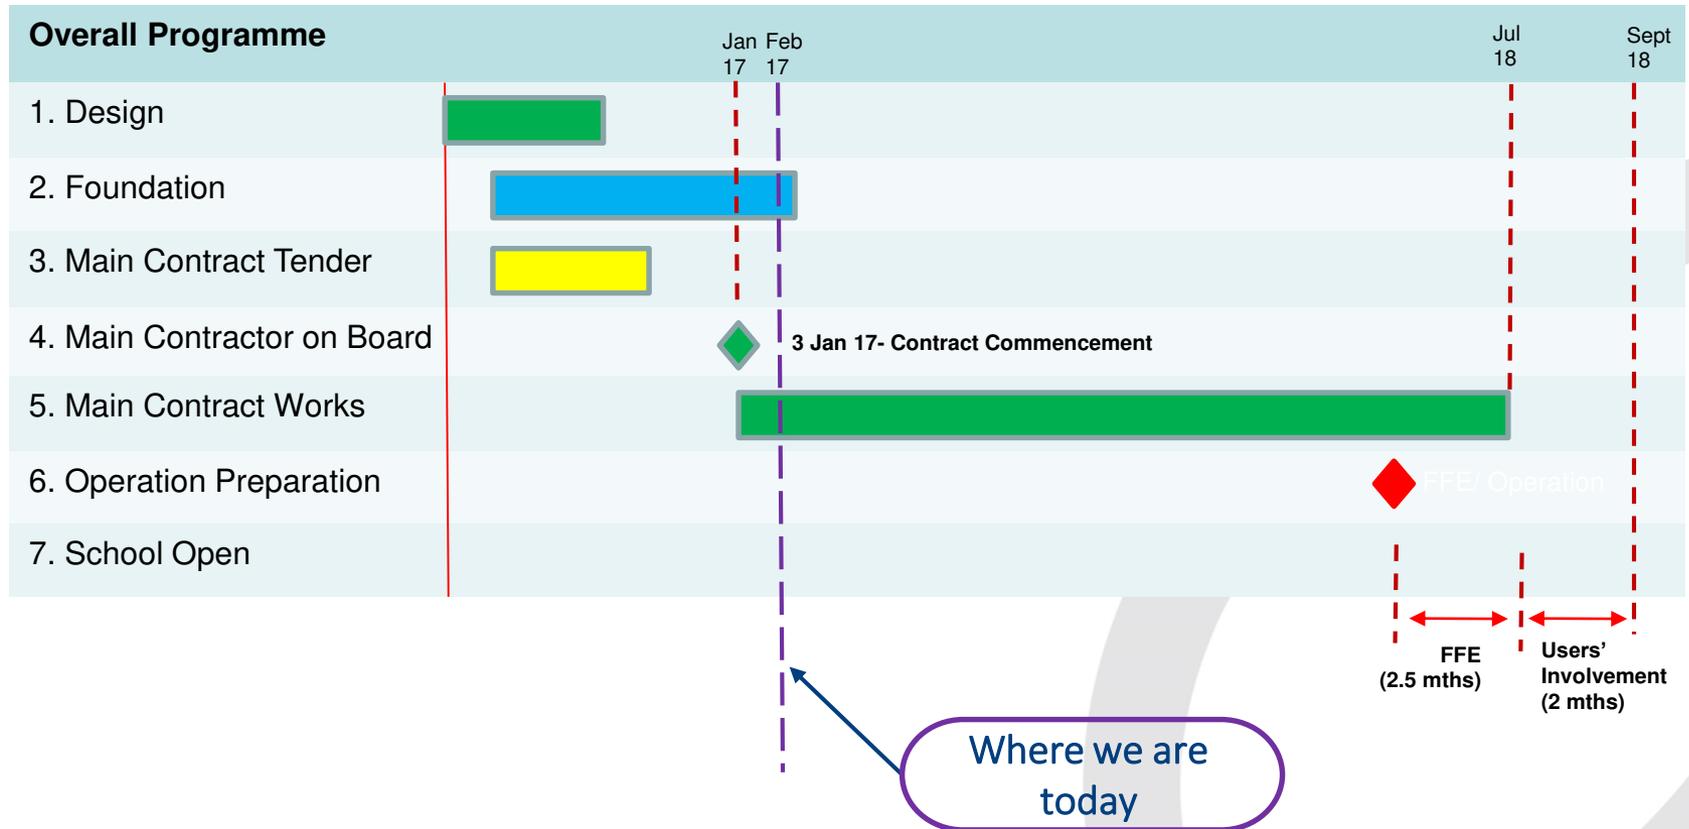

TKO Project Progress Update

Key Achieved Milestones:

- 1) Foundation Work Commencement - 1 Jun 16
- 2) Foundation Works Completion – 16 Feb 17
- 3) Main Works Contract Commencement with Primary School Construction – 3 Jan 17
- 4) Secondary School Construction Commencement – 17 Feb 17



Upcoming Key Milestones:

- 1) *Premiere Pierre* – 26 April 17
- 2) School Buildings Completion – 16 Feb 18
- 3) Main Works Completion- 30 Jun 18

Merci / Thank you

Questions?

Email us at:

tkocampus@lfis.edu.hk

